

Work Order ID 133970

Tuesday, June 23, 2015 3:26:01 PM

133970

Page 1

Item ID: D4149-1 Accept ***N900040100*** Setup Start ***NS1***
Revision ID: Stop ***NS2***
Item Name: Crosstube Lug Plate, Aft
Start Date: 6/23/15 Start Qty: 8.00 ***8*** Cust Item ID:
Required Date: 6/23/15 Req'd Qty: 8.00 ***8*** Customer:
Reference:

Approvals: Process Plan: MLS Date: JUN 24 2015 Tooling: _____ Date: _____
QC: _____ Date: _____ SPC (Y/N): _____ Date: _____
Run Start ***NR1***
Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D4149	C								

100

0.00

100

Waterjet

FLOW CNC Waterjet

304-125**Memo**

Cut as per dwg D4149

Prog Rev: CDwg Rev: C

OPEN TO HOLES TO FINISH SIZE AS PER DWG

Deburr as required

8 Ø Jm15-6-25

110

QC2- Inspect parts off machine FAI/FAIB

0.00

110

QC

Quality Control

Memo

0.00

8 Ø Jm15-6-25

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : ☐					

Work Order ID 133970

Tuesday, June 23, 2015 3:26:01 PM

133970

Page 2

Item ID: D4149-1

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Crosstube Lug Plate, Aft

Start Date: 6/23/15 Start Qty: 8.00

g

Cust Item ID:

Required Date: 6/23/15 Req'd Qty: 8.00

g

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Run Start ***NR1***Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
120	QC8- Inspect parts - second check	0.00				<u>8</u>			DAS 38 9-89
120									
QC	Memo	0.00							
Quality Control									JUN 25 2015
150	Identify as per dwg & Stock Location: <u>9094</u>	0.00							
150									
Packaging	Memo	0.00							<u>CL</u> <u>15/06/26</u> <u>8</u>
Packaging									
160	QC21- Final Inspection - Work Order Release	0.00							
160									
QC	Memo	0.00							<u>MLJ</u> <u>JUN 29 2015</u>
Quality Control									

MLJ JUN 29 2015

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QSI042) Approval	
Description Work Order Deviation			Disposition		
			Completed By		
			Lead hand / Supervisor Approval Verification		
			QC / QA Coordinator Approval		
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Mislabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : ☐					

Picklist Print

Tuesday, June 23, 2015 3:26:00 PM

Page 1

Work Order ID: 133970

133970

Parent Item: D4149-1

D4149-1

Parent Item Name: Crosstube Lug Plate, Aft

Start Date: 6/23/15

Required Date: 6/23/15

Start Qty: 8.00

Required Qty: 8.00

Comments: IPP Rev:A 10.06.24 new issue DD verf:EC
IPP Rev:B 11.03.03 as per revC DD verf:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
M304S11GA		Purchased			No	100	sf	161.0257	0.1355	1.141053			
M304S11GA									**	(1.5)		Jm 15-6-25	
304/316 0.125 Sheet													

Location

Loc Qty

Loc Code

MAT020

161.0257

122521

40.034

M128254

56

M129545

36.575

M129972

28.4167

129972.

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____	DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐	AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐			
Date :	Step #:	QTY Effective :		MRB (QS1042) Approval	
Description Work Order Deviation		Disposition		Completed By	
				Lead hand / Supervisor Approval Verification	
				QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY			
Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐	No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐	Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐	Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐	Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐	Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐
OTHER : ☐					


DART AEROSPACE LTD		Work Order: 133970
Description: Aft Crosstube Lug Plate		Part Number: D4149-1
Inspection Dwg: D4149	Rev: C	Page 1 of 1

FIRST ARTICLE INSPECTION CHECKLIST

Drawing Dimension	Tolerance	Actual Dimension	Accept	Reject	Method of Inspection	Comments
Ø0.129	+0.005/-0.001	0.130"	-		✓	Items
Ø0.191	+0.005/-0.001	0.193"	-		✓	
Ø0.257	+0.006/-0.001	0.258"	-		✓	
Ø0.38	+0.006/-0.001	0.38"	-		✓	
0.380	+/-0.010	0.380"	-		✓	
0.469	+/-0.010	0.469"	-		✓	
0.310	+/-0.010	0.310"	-		✓	
0.750	+/-0.010	0.750"	-		✓	
3.25	+/-0.030	3.25"	-		✓	
0.65	+/-0.030	0.65"	-		✓	
0.63	+/-0.030	0.63"	-		✓	
5.46	+/-0.030	5.46"	-		✓	
3.80	+/-0.030	3.80"	-		✓	
2.13	+/-0.030	2.13"	-		✓	
1.313	+/-0.010	1.313"	-		✓	
0.625	+/-0.010	0.625"	-		✓	
0.375	+/-0.010	0.375"	-		✓	
1.175	+/-0.010	1.175"	-		✓	
0.752	+/-0.010	0.752"	-		✓	
1.588	+/-0.010	1.588"	-		✓	
1.587	+/-0.010	1.587"	-		✓	
11.15	+/-0.030	11.15"	-		T	
0.750	+/-0.010	0.750"	-		✓	
1.55	+/-0.030	1.55"	-		✓	
1.12	+/-0.030	1.12"	-		✓	
8.42	+/-0.030	8.42"	-		✓	
2.70	+/-0.030	2.70"	-		✓	
0.125	+/-0.010	0.125"	✓		✓	
Ø0.252	+0.003/-0.000	0.252"	-		✓	

Measured by: JM	Audited by: DAS	Preliminary Approval:
Date: 15-6-15	Date: 9-89	Date:

Rev	Date	Change	Revised by	Approved
A	10.08.04	New Issue	KJ	
B	12.02.01	Dimensions updated per Dwg Rev C	KJ	

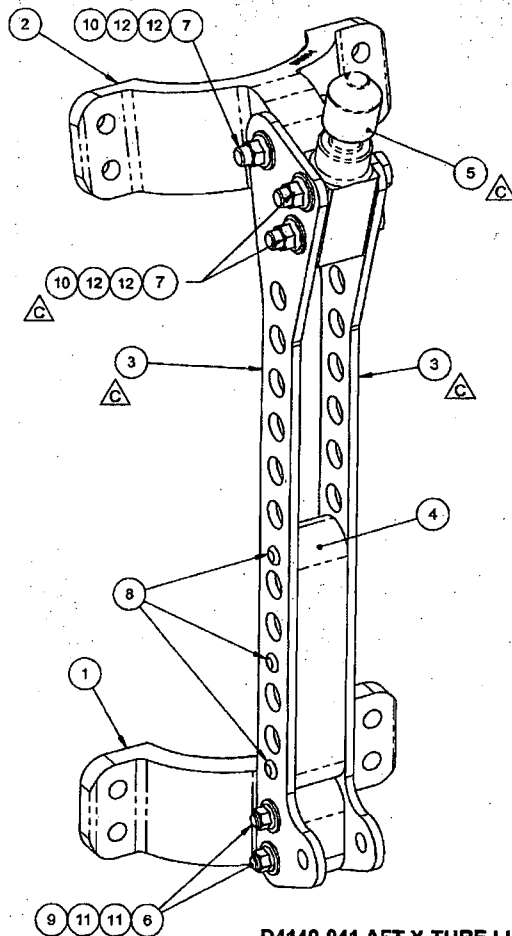

D4149-041 AFT X-TUBE LUG ASSY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: N/A
- 6) IDENTIFICATION: IDENTIFY WITH DART P/N "D4149-041" USING FINE POINT PERMANENT INK MARKER
- 7) WEIGHT: 2.21 lbs

ITEM	QTY -041	P/N	DESCRIPTION
	X	D4149-041	AFT X-TUBE LUG ASSY
1	1	D3910-1	X-TUBE LUG
2	1	D4091-1	MOUNTING LUG
3	2	D4149-1	AFT X-TUBE LUG PLATE
4	1	D4149-3	SPACER
5	1	D4149-5	EYEBOLT STUD
6	2	AN3C12A	BOLT
7	3	AN4C13A	BOLT
8	3	MS20815-4M18	RIVET
9	2	MS21043C3	NUT
10	3	MS21043C4	NUT
11	4	NAS1149C0332R	WASHER
12	6	NAS1149C0432R	WASHER

SHIP COPY

RETURN TO

ENGINEERING



133930 MJS

15-0624 11 2011-02-26

RELEASED

C	HOLE DIA CHANGED TO 0.252" (D8-3); HOLE DIA CHANGED TO 0.250" (C2-5); REPLACED QTY(2) AN3C12A, MS21043C3 AND QTY(4) NAS1149C0332R WITH QTY(2) AN4C13A, MS21043C4 AND QTY(4) NAS1149C0432R (D3-1, D7-2)	SC	11.02.22
B	MS20815-4M18 WAS MS20815-4M20 (ZN D3-1 & B7-2); ADDED D4149-5 (SHT 5); D4149-5 WAS D3909-5 (ZN D3-1 & D7-2); REPLACED QTY(5) MS20815-4M18 WITH QTY(2) EACH AN3C12A, MS21043-3 AND QTY(4) NAS1149C0332R WASHER (ZN D3-1, C7-1, B7-2 & B3-2); Ø0.191 2 PL REPLACES Ø0.129 3 PL (ZN D6-3) REASON: SEE TR-D350-607-2 REV. B.	MB	10.07.05
A	NEW ISSUE	MB	10.06.18
REV.	DESCRIPTION	BY	DATE
DESIGN	MB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	SC		
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 1 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2018 BY DART AEROSPACE LTD THIS DOCUMENT IS PROPRIETARY AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE REPRODUCED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8 7 6 5 4 3 2 1

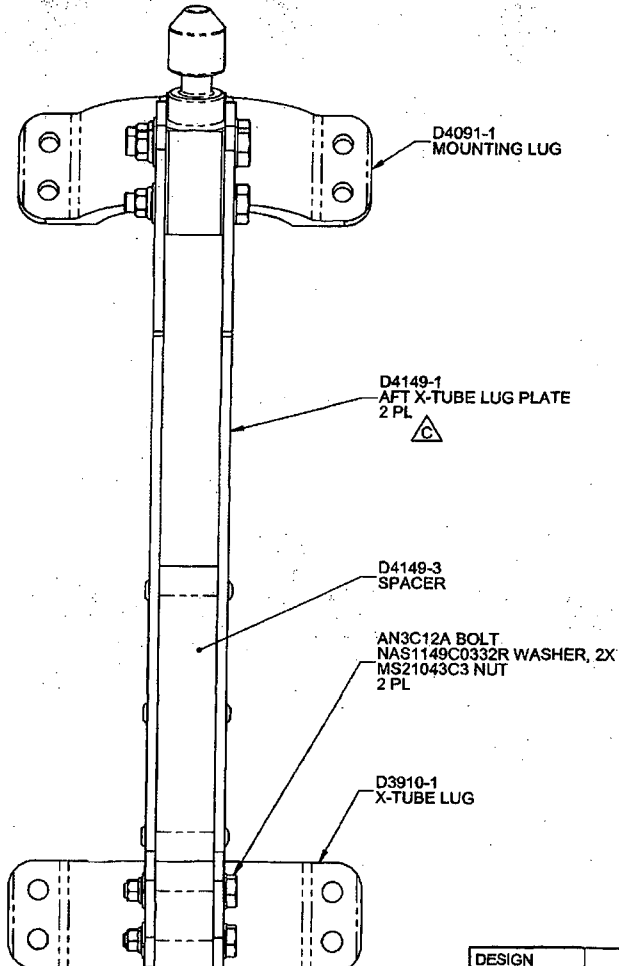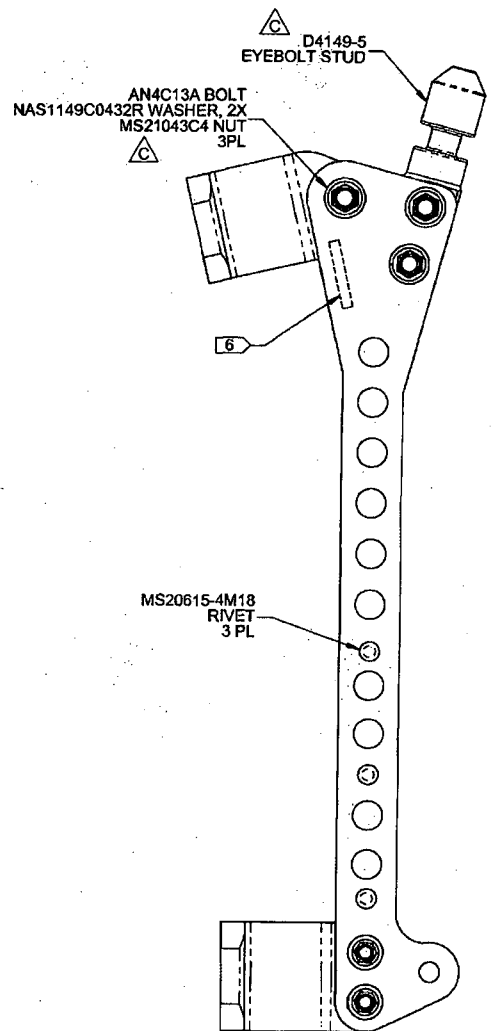





D4149-041 AFT X-TUBE LUG ASSY

RELEASED
2011-02-24
MP

DESIGN	MB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	SC		
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 2 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR REPRODUCED IN ANY MANNER WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

8 7 6 5 4 3 2 1

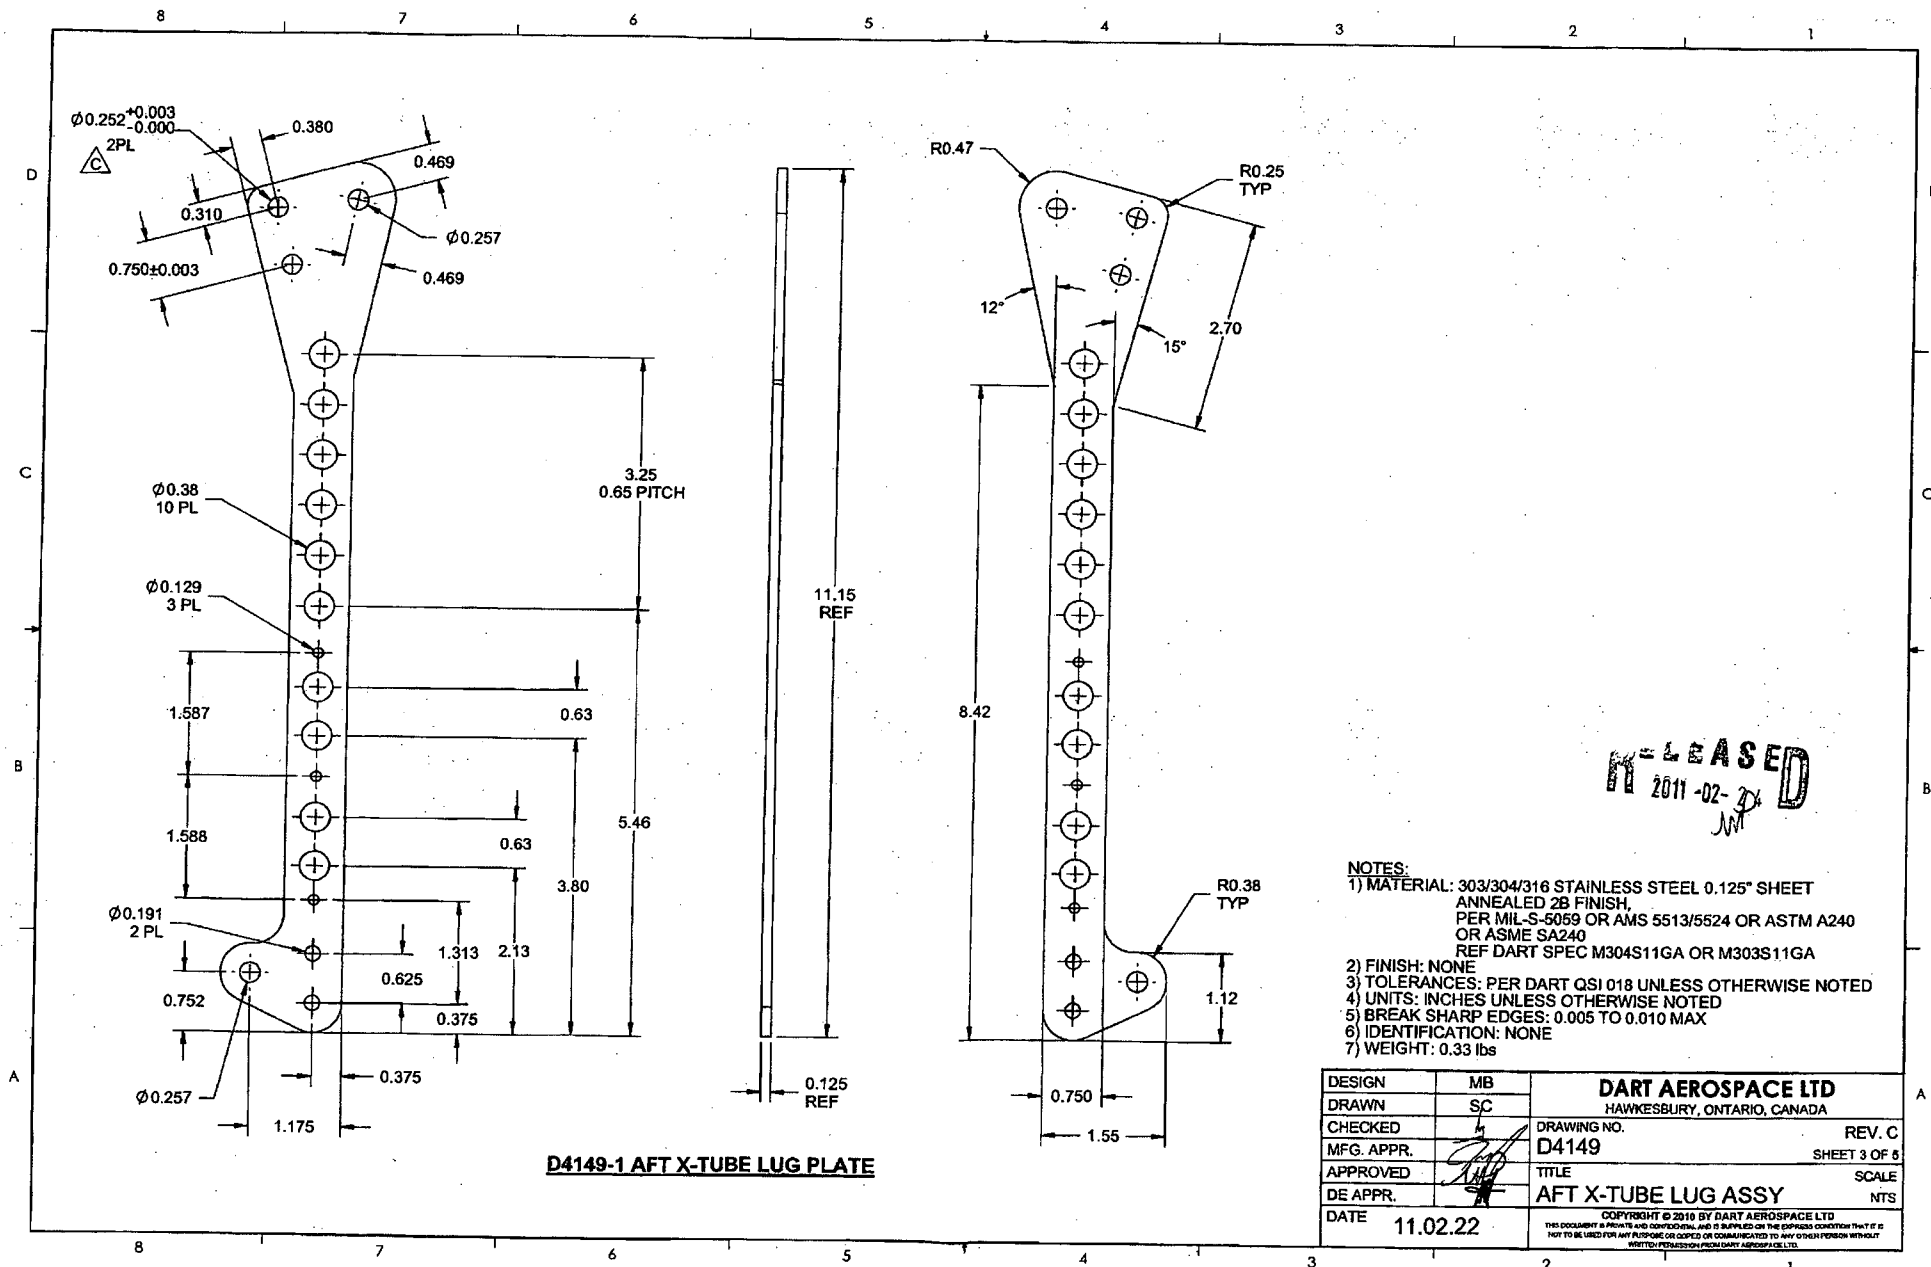

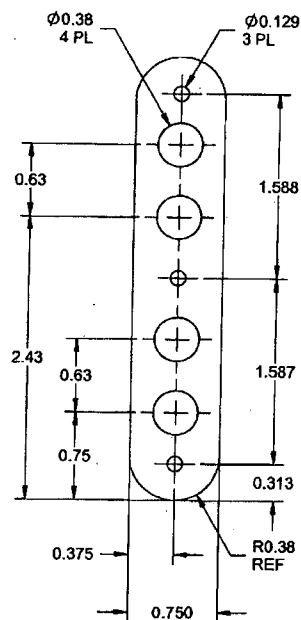



D4149-3 SPACER

RELEASED
2011-02-24

NOTES:

- 1) MATERIAL: 303/304/316 STAINLESS STEEL BAR PER ASTM A276 OR A582
REF DART SPEC MS304B OR MS303B
- 2) FINISH: NONE
- 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK ALL SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: 0.47 lbs

DESIGN	MB	DART AEROSPACE LTD	
DRAWN	SC	HAWKESBURY, ONTARIO, CANADA	
CHECKED		DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 4 OF 6
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSES OR COPIED OR DISSEMINATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			

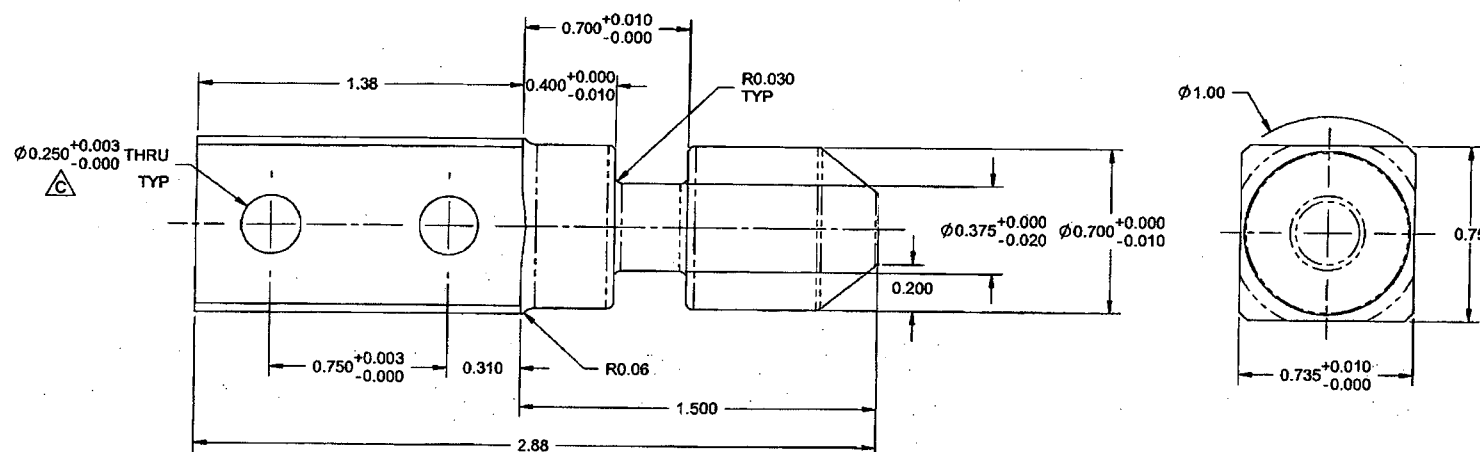

D4149-5 EYEBOLT STUD

RELEASED
2011-02-24

- NOTES:**
- 1) MATERIAL: 303/304/316 STAINLESS STEEL BAR PER ASTM A276 OR A582
REF DART SPEC MS304B OR MS303B
 - 2) FINISH: NONE
 - 3) TOLERANCES ARE PER DART QSI 018 UNLESS OTHERWISE NOTED
 - 4) UNITS: INCHES UNLESS OTHERWISE NOTED
 - 5) BREAK ALL SHARP EDGES: 0.005 TO 0.010 MAX
 - 6) IDENTIFICATION: IDENTIFY WITH DART P/N "D4149-5" USING FINE POINT PERMANENT INK MARKER
 - 7) WEIGHT: 0.32 lbs

DESIGN	MB	DART AEROSPACE LTD	
DRAWN	SC	HAWKESBURY, ONTARIO, CANADA	
CHECKED	A	DRAWING NO.	REV. C
MFG. APPR.		D4149	SHEET 5 OF 5
APPROVED		TITLE	SCALE
DE APPR.		AFT X-TUBE LUG ASSY	NTS
DATE	11.02.22	COPYRIGHT © 2010 BY DART AEROSPACE LTD	
THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.			
